

Asmita — Implementation Plan

Version: 0.1 **Date:** 2026-05-12 **Status:** Pre-development **Derived from:** PRD_Asmita.md v0.2 · TRD_Asmita.md v0.1

*This document is about **sequencing and ownership** — not a restatement of features. Feature specs live in the PRD; technical requirements in the TRD. Consult those for what to build; this document for when, in what order, and who must unblock whom.*

Table of Contents

1. Assumptions & Preconditions
2. Critical Path
3. Workstream Lanes
4. Pre-Development Phase (Week -4 to 0)
5. Month 1 — Foundation
6. Month 2-3 — Core Build
7. Month 4 — Soft Launch (Closed Beta)
8. Month 5-6 — Hardening & Public Launch
9. Pre-Launch Non-Code Checklist
10. Deferred-Decision Resolution Schedule
11. Dependency Map (Key Blockers)
12. Risk Register
13. Phase 2 Gate Condition

1. Assumptions & Preconditions

The plan below assumes the minimum team from PRD §17:

Role	Time commitment
Product Owner (Founder)	Part-time
Backend Developer	Full-time, Months 1-6
Frontend Developer	Full-time, Months 2-6
Legal Advisor (cyber law)	Part-time retainer; 2-4 hrs/week
NGO Outreach Lead	Part-time
Hindi Translator	Freelance, Month 2-3


If any of these roles are not staffed before Month 1 begins, adjust the plan accordingly — do not start Month 1 engineering work without the Backend Developer in place.

Hard preconditions (nothing starts without these)

- **Funding secured (D-05):** Minimum 3–4 months of funded development. This is Week –4 to 0. No Month 1 milestone is achievable without it. See §4.
- **Legal advisor retained:** Notice templates cannot be drafted without legal review. Retainer must be signed before Month 1 ends.
- **Legal entity decision (D-01):** Section 8 company / trust / NGO. Must be decided and filing initiated before Month 4 soft launch. Notices sent from an unregistered entity carry less legal weight.

2. Critical Path

The longest chain of must-complete-before-X steps that sets the minimum time to public launch:

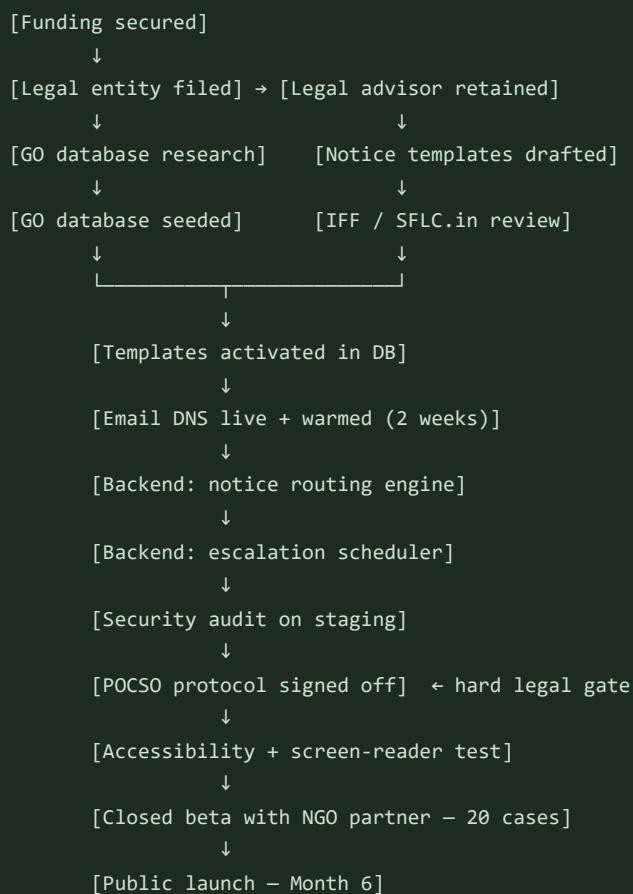

What slips the date:

- IFF/SFLC.in review delayed (external dependency — outreach must start Week 1)
- POCSO protocol not drafted (same legal advisor, capacity conflict — see §4)
- GO database has placeholder contacts at Month 4 (TRD Appendix B: no placeholders at launch)
- Email DNS not warmed before Month 4 (2-week fixed calendar cost)

3. Workstream Lanes

Six parallel workstreams. Each lane runs independently; dependencies between them are listed in §11.

Lane	Owner	Runs
E — Engineering	Backend Dev + Frontend Dev	Month 1–6
L — Legal Review	Legal Advisor	Month 1–6 (part-time)
G — GO Research	NGO Outreach Lead or dedicated researcher	Week 1–Month 2
N — NGO Outreach	NGO Outreach Lead	Month 1–4
T — Translation	Hindi Translator + Legal Advisor review	Month 2–3
O — Ops / Infra	Product Owner + Backend Dev	Month 1 setup; ongoing

Engineering cannot do GO research, translation, or NGO outreach. These lanes must have dedicated owners from Day 1.

4. Pre-Development Phase (Week –4 to 0)

These are not engineering tasks. They are founder/product-owner tasks that must complete before the engineering clock starts.

Task	Owner	Done-when
Funding secured	Founder	Committed funding for 4 months of team cost
Legal entity decision (D-01)	Founder + Legal Advisor	Entity type chosen; filing initiated
Legal advisor retainer signed	Founder	Signed contract; first briefing done
Legal advisor briefed on: POC SO scope, notice template review, DPDP alignment	Founder + Legal Advisor	Briefing call completed; advisor has PRD + TRD
D-06 (POCSO protocol) kicked off	Legal Advisor	Draft scope agreed; timeline set
AWS account created; ap-south-1 region selected; billing alerts set	Product Owner	Account live
IFF / SFLC.in first outreach email sent	Founder	Email sent, response awaited
GO research brief written and researcher assigned	Product Owner	Researcher has brief + platform list (TRD Appendix B)
NGO partner outreach initiated (iCall, Cyber Peace Foundation)	NGO Outreach Lead	At least one NGO in conversation
D-02 (anonymous vs. registered), D-03 (languages), D-04 (supporter) decided	Founder + Product Owner	Decisions documented; TRD §18 updated

Gate to Month 1: Funding confirmed + legal advisor retained + AWS account live + D-02/D-03/D-04 resolved.

5. Month 1 — Foundation

Goal: Infrastructure live, database schema deployed, GO database seeded for Tier 1 platforms, notice templates drafted and in legal review.

E — Engineering

Week	Task	TRD Ref
1	Dev environment setup; repo structure; CI/CD pipeline skeleton (GitHub Actions / equivalent)	INFRA-02, INFRA-05
1	Write the no-fetch invariant CI test first — before any URL-handling code	NFI-01, §16.4
1–2	PostgreSQL schema deployed on staging: <code>victims</code> , <code>cases</code> , <code>submitted_urls</code> , <code>platforms</code> , <code>notices</code> , <code>escalations</code> , <code>audit_log</code> , <code>notice_templates</code> , <code>platform_go_history</code>	§5.1
1–2	KMS key created; field-level encryption helpers written and tested	§5.2, PRIV-02
2–3	Auth service: OTP generation, email OTP flow, session token issuance (no passwords)	AUTH-01 – AUTH-06, FR-REG-01, FR-REG-02
2–3	Sending domain configured: SPF, DKIM, DMARC records published; Postmark/Resend account created; IP warm-up started	EMAIL-01 – EMAIL-06
3–4	URL parser: domain extraction, platform lookup, rate-limiting middleware	FR-URL-01 – FR-URL-04, ABU-03
3–4	Admin panel scaffolding: RBAC roles, login, GO database editor UI	FR-ADMIN-01, FR-ADMIN-05
4	Abuse detection signals: flagging rules, review queue endpoint	ABU-04, FR-ADMIN-02

L — Legal Review

Task	Done-when
Draft Template A (Indian IT Rules 2021)	First draft submitted to IFF/SFLC.in
Draft Template B (International DMCA + Indian law)	First draft submitted
Draft Template C (Pornographic platforms, DMCA primary)	First draft submitted
IFF / SFLC.in engagement confirmed	Response received; review timeline set
D-06: POCSO protocol first draft	Draft written by legal advisor

Warning: IFF and SFLC.in have their own timelines. Do not assume review in under 4 weeks. Plan for 6 weeks. First outreach was Week -4; follow up Week 1.

G — GO Research

Task	Done-when
All Tier 1 platforms (8 platforms, TRD Appendix B): GO contact verified via platform's own Terms/Contact page	Contact email + last-verified date recorded

Task	Done-when
All Tier 2 platforms (Pornhub/Aylo, xVideos, xHamster, XNXX, RedTube): abuse/DMCA form URL verified	Form URL + process notes recorded
Tier 3 (Search engines): removal tool URLs verified	Recorded
Each entry entered in GO database with verification source	Admin panel shows no <code>is_stale</code> entries

*GO research is **not** a sprint ticket. It is a 4–6 week parallel workstream requiring daily researcher time and direct verification from each platform's live site (not from cached sources).*

N — NGO Outreach

Task	Done-when
iCall (TISS) partnership discussion initiated	Meeting scheduled
Cyber Peace Foundation discussion initiated	Meeting scheduled
Red Dot Foundation discussion initiated	Meeting scheduled
At least one NGO partner confirmed for Month 4 beta	MOU or written agreement

Month 1 Gate (must all be true before Month 2 engineering begins):

- ☐ Database schema deployed on staging and reviewed by Backend Dev
- ☐ No-fetch invariant CI test is live and green
- ☐ Auth service passes integration tests (OTP register → verify → session)
- ☐ Email sending domain live with SPF/DKIM/DMARC; warm-up in progress
- ☐ GO database seeded for all Tier 1 platforms (no placeholder contacts)
- ☐ Notice templates in legal review (IFF/SFLC.in)
- ☐ D-02, D-03, D-04 decisions documented

6. Month 2–3 — Core Build

Goal: Full notice routing engine, escalation scheduler, victim dashboard, admin panel complete. Hindi translation delivered and reviewed. Templates legally approved and activated.

E — Engineering

Month 2:

Task	TRD Ref
Victim registration form (email OTP + age attestation + declaration)	FR-REG-01 – FR-REG-07
Minor pathway: hard branch, no data storage, all referral content	FR-MIN-01 – FR-MIN-04
URL submission form: input, local parse, platform lookup, rate-limit UI	FR-URL-01 – FR-URL-06
Notice generation engine: template selection, variable substitution, notice record creation	FR-NR-02, FR-NR-06

Task	TRD Ref
Tier 2 notice dispatch: email send via Postmark/Resend with idempotency key	FR-NR-01, FR-NR-04
Bounce/complaint webhook receiver wired to platform <code>is_stale</code> flag	EMAIL-04, EMAIL-05
Append-only audit log: DB policy enforced + all required events logged	AUDIT-01, AUDIT-02

Month 3:

Task	TRD Ref
Escalation scheduler (background worker): T+24h, T+48h, T+7d; idempotency; UTC clock source	FR-ESC-01 – FR-ESC-05
7-day legal package PDF generation (Devanagari font embedded)	FR-ESC-05, I18N-04
Case tracking dashboard: per-URL status, add URLs, manual resolve, PDF export	FR-DASH-01 – FR-DASH-06
Admin panel: review queue, notice template editor, platform response rate dashboard	FR-ADMIN-02 – FR-ADMIN-04
Victim confirmation email (case ref + dashboard link, no URLs)	FR-NR-05
Tier 3 web form handoff: instructions, pre-filled template, victim confirmation	FR-NR-08
Tier 1 API client for Meta (if API partnership confirmed) + Google removal	FR-NR-07; mark as Tier 2 fallback if partnership not confirmed
Aadhaar offline XML verification (signature check against bundled UIDAI cert chain)	FR-REG-05, ABU-06
Account deletion flow (soft delete + 30-day hard delete job)	FR-DASH-06, PRIV-07

L — Legal Review

Task	Done-when
IFF / SFLC.in review of all three templates completed	Written sign-off received
Templates entered in DB with <code>reviewed_by</code> set; legal advisor activates via admin panel	<code>notice_templates.reviewed_at</code> not null
POCSO protocol finalised and documented	Written protocol signed by legal advisor
D-01: Legal entity registered	Registration filing confirmed

POCSO protocol must be complete before Month 4 soft launch. This is a hard gate per TRD FR-MIN-05. The legal advisor drafting this is the same person reviewing templates — flag the capacity conflict to the founder by end of Month 1.

T — Translation

Task	Done-when
All UI strings translated to Hindi by qualified translator	Translator delivers string file
All legal citations and declaration text translated and reviewed by legal advisor	Legal advisor signs off Hindi legal text
Hindi notice templates (A, B, C) translated and reviewed	Templates in DB with Hindi body
Support resources page content translated	Content in CMS / string file

N — NGO Outreach

Task	Done-when
NGO partner for beta confirmed and briefed on the platform	MOU signed; partner has access to staging
NGO vouching API documented and shared with partner	API key issued to partner
20 potential beta cases identified through NGO partner	Partner has list ready for Month 4

Month 2–3 Gate (must all be true before Month 4 beta):

- ☐ Full victim flow works end-to-end on staging: register → declare → submit URL → notice dispatched → dashboard shows status
- ☐ Minor pathway integration test passes (zero rows written to database)
- ☐ Escalation scheduler fires correctly at T+24h and T+48h in staging environment
- ☐ 7-day legal package PDF renders correctly in Hindi and English with all required fields
- ☐ Notice templates activated in DB (legal advisor review complete)
- ☐ POCSO protocol document signed by legal advisor
- ☐ Hindi UI fully translated and reviewed
- ☐ Email IP warm-up complete; test deliverability to major Indian providers (Gmail, Hotmail, Yahoo)
- ☐ Admin panel: all RBAC roles working; GO database editor functional

7. Month 4 — Soft Launch (Closed Beta)

Goal: Process 20 real victim cases with NGO partner oversight. Validate notice delivery, platform responses, escalation logic, and victim UX under real conditions.

Pre-Beta Checklist (must complete before first real case)

- ☐ Security audit on staging (see §9 — NFR-SEC-05)
- ☐ Accessibility test: WCAG 2.2 AA + screen-reader pass (NVDA / VoiceOver)
- ☐ Legal entity registration confirmed (not just filed)
- ☐ All Tier 1 + Tier 2 platform contacts verified and current in GO database
- ☐ Email DNS fully configured; DMARC policy `p=quarantine` active
- ☐ Founder has reviewed and approved the live notice templates
- ☐ NGO partner briefed; NGO API key issued; vouching workflow tested
- ☐ Victim deletion flow tested on staging (30-day cycle simulated)

- ☐ On-call alert routing configured (OBS-03)
- ☐ DR test: simulated RDS failure; recovery confirmed within RTO

E — Engineering (Month 4)

Task	Notes
Deploy to production (ap-south-1)	Final prod environment check
Bug fixes from beta cases	Triage daily with NGO partner
Platform response tracking: log all acknowledgments and removals from real cases	Feeds response-rate dashboard
Monitor email deliverability metrics daily	Bounce rate < 2%; spam < 0.1%
Monitor escalation scheduler: confirm T+24h/T+48h fires on real cases	

Data to collect during beta (feeds Phase 2)

Metric	Target to measure
Notice delivery success rate per platform	% delivered, % bounced
Platform acknowledgment rate	% within 24h, 48h, 7 days
Content removal rate	% removed within 72h
Victim time-on-task (registration → first notice sent)	Target < 15 minutes
Cases where victim requested escalation package	Qualitative feedback

Month 4 Gate:

- ☐ 20 beta cases processed without data breach or privacy incident
- ☐ No notice sent to a wrong platform contact (GO database accuracy)
- ☐ Escalation scheduler fired correctly on all cases with no-response
- ☐ At least one platform acknowledged a notice
- ☐ Zero cases where the no-fetch invariant was violated (audit log confirms)
- ☐ Victim feedback collected (survey or NGO debrief)

8. Month 5–6 — Hardening & Public Launch

Goal: Fix issues from beta. Reach 100 cases processed. Public launch Month 6.

Month 5 — Hardening

Lane	Task
E	Fix all P1/P2 bugs from Month 4 beta
E	Performance: Lighthouse CI passing LCP ≤ 3s, JS ≤ 200KB
E	DMARC upgrade from <code>p=quarantine</code> to <code>p=reject</code> (after 30 days monitoring)

Lane	Task
E	Load test on staging: 100 concurrent submissions (TRD NFR-AVAIL-01)
E	Hash-chaining on audit log (TRD AUDIT-03 — required before legal package feature is relied upon)
L	Review any notice template changes indicated by beta response data
L	DPDP implementation rules check: any new rules notified since pre-dev?
G	Update any GO contacts that bounced during beta
N	Expand NGO partner network; onboard second NGO
O	Response rate dashboard reviewed: identify lowest-response platforms for different escalation strategy

Month 6 — Public Launch

Task	Owner	Done-when
Soft-remove "beta" labels from UI	Frontend Dev	UI updated
Press/announcement to NGO network	NGO Outreach Lead	Announced
Public launch blog/FAQ page (in Hindi + English)	Product Owner + Translator	Live
Support resources page verified current (helpline numbers, DLSA directory)	NGO Outreach Lead	Verified
100-case milestone tracking begins	Product Owner	Dashboard live
Monthly GO database verification schedule established	GO Research owner	First review done

Public Launch Gate (hard — all must be true):

- ☐ 20+ beta cases closed (removed or escalation package delivered)
- ☐ No open P1 security or privacy bugs
- ☐ POC SO protocol document signed and stored
- ☐ Legal entity registered and active
- ☐ Notice templates legally reviewed and active (all three types)
- ☐ GO database: zero placeholder contacts, zero stale entries
- ☐ Email: DMARC `p=reject` ; bounce rate < 2%
- ☐ Audit log hash-chaining live
- ☐ Accessibility: WCAG 2.2 AA certified
- ☐ Victim deletion flow verified on production (test account)
- ☐ DR test passed on production infrastructure

9. Pre-Launch Non-Code Checklist

These items are not GitHub tickets. Each needs an owner and a completion date.

Item	Owner	Blocks
Legal entity registered	Founder	Notice credibility; public launch
Legal advisor retainer active	Founder	Template review; POCSO protocol
IFF or SFLC.in notice template review completed	Legal Advisor	Template activation
POCSO reporting protocol written and signed	Legal Advisor	Production deployment
All Tier 1 + Tier 2 GO contacts verified (no placeholders)	GO Researcher	Notice routing; soft launch
SPF + DKIM + DMARC published for sending domain	Ops	Any email notices sent
Email IP warm-up completed	Ops	Any email notices sent
Security audit on staging	Backend Dev / External	Soft launch
Accessibility test (WCAG 2.2 AA + screen reader)	Frontend Dev	Public launch
Hindi legal text reviewed by legal advisor	Legal Advisor + Translator	Hindi template activation
DR test (RDS recovery within RTO)	Backend Dev	Public launch
NGO partner MOU signed	NGO Outreach Lead	Soft launch
DPDP compliance check (once implementation rules notified)	Legal Advisor	Ongoing — track as standing obligation
Monthly GO database re-verification cadence assigned	Product Owner	Post-launch operations
Victim feedback collection mechanism in place (survey or NGO debrief)	Product Owner	Month 4 beta

10. Deferred-Decision Resolution Schedule

From TRD §18. Each decision blocks specific engineering work. Resolving late forces rework.

Decision	Must resolve by	Blocks if delayed
D-01 — Legal entity type	End of Month 2 (file by Month 1)	Notice credibility; funding eligibility
D-02 — Anonymous vs. registered submissions	End of Week –1 (pre-dev)	Auth model; if anonymous, major TRD rework
D-03 — Languages at launch (Hindi+English or add third)	End of Week –1	Translation scope; add 2+ weeks if third language added
D-04 — Supporter pathway Day 1 or post-launch	End of Month 1	FR-REG-08; consent form upload; if post-launch, drop from Phase 1 scope
D-05 — Funding secured	Before Week 1 (pre-dev gate)	Everything
D-06 — POCSO reporting protocol	Before Month 4 soft launch	Production deployment; hard legal gate

Decision	Must resolve by	Blocks if delayed
D-07 — GO database maintenance owner (post-launch)	By Month 3	Month 4 beta: stale contacts = failed notice delivery
D-08 — Non-response escalation playbook	By Month 3	Escalation scheduler operational configuration

11. Dependency Map (Key Blockers)

For each major system component, what must be complete first.

Component	Blocked by
Notice dispatch (FR-NR-01)	Email DNS live + warmed; GO database seeded; templates legally reviewed and activated
Template activation	IFF/SFLC.in legal review complete; legal advisor signs off in DB
Escalation scheduler (FR-ESC)	Notice dispatch working; clock source confirmed (UTC DB time)
Minor pathway (FR-MIN)	POCSO protocol signed; hard branch verified by integration test
Aadhaar KYC (FR-REG-05)	UIDAI cert chain bundled; signature verification unit-tested
7-day legal package PDF	PDF renderer with Devanagari font tested; Hindi translation reviewed
Soft launch	Security audit; accessibility test; GO database complete; templates active; NGO partner confirmed
Public launch	Soft launch gate passed + all pre-launch checklist items
Phase 2 (hash network)	100+ Phase 1 cases processed; per-platform response rates documented

12. Risk Register

Inherits risks from PRD §18 with owners and trigger dates added.

Risk	Severity	Trigger date	Owner	Mitigation
IFF/SFLC.in review delayed >6 weeks	High	Month 2 end	Legal Advisor	Follow up weekly; identify backup reviewer (cyber law practitioner with IT Rules experience) by Month 2 if no response
GO contact bounces after notice sent	High	Month 4 (beta)	GO Researcher	Bounce webhook flags entry as <code>is_stale</code> ; re-verify within 24h; manual notice resent
POCSO protocol not ready by Month 4	High	Month 3 end	Legal Advisor	Escalate to founder; consider delaying soft launch rather than launching without it
Legal entity not registered by Month 4	Medium	Month 3 end	Founder	File by Month 1; track registration status weekly

Risk	Severity	Trigger date	Owner	Mitigation
Email notices land in spam	High	Month 3 (warm-up)	Backend Dev	Monitor inbox placement during warm-up; adjust sending volume; consider dedicated IP
D-02 left as anonymous → auth model requires significant rework	High	Week -1	Founder	Resolve in pre-dev phase; default to registered (OTP) per PRD recommendation
Abuse case: bad actor submits legitimate URL as NCII	High	From Month 4	Case Reviewer	Human review queue SLA 4h; abuse detection signals (ABU-04) must be live before soft launch
Minor content submitted through adult pathway	Critical	From Month 4	Engineering	Age attestation hard branch live; POCSO protocol in place; no workaround
Data breach exposing victim information	Critical	Ongoing	Backend Dev	Field-level encryption; no content stored; security audit pre-launch; quarterly review
Supporter pathway (D-04) deprioritised creates victim access gap	Medium	Month 1 decision	Product Owner	If deferred, document clearly; NGO partners can still vouch (FR-ADMIN-06)
Phase 2 partnership conversations stall because Phase 1 data is thin	Medium	Month 6	Product Owner	Publish platform response rate data publicly to create accountability pressure

13. Phase 2 Gate Condition

Phase 2 (hash network) does not start until **both** conditions are met:

1. **100+ Phase 1 cases processed** with documented per-platform response rates (PRD §14, §15)
2. **Phase 1 infrastructure is stable** — no open P1 bugs; escalation scheduler running without manual intervention for 30+ days

The per-platform response rate data from Phase 1 is the basis for every Phase 2 platform partnership conversation. Starting Phase 2 conversations without it is the wrong sequence.

Phase 2 technical design is not in scope for this document. See PRD §14 Phase 2 for feature scope; TRD §17 for Phase 1 extension points.

Document Owner: [Product Owner / Founder] Last Updated: 2026-05-12 Derived from: PRD_Asmita.md v0.2 · TRD_Asmita.md v0.1 Next Review: End of Month 1 (update with actual dates and staffing)
